Sprint 1 Materials

Team 80 Chud-maxxing

Joaquin A. Zapata
Vincent Yen
Ryan Kappil
Landon ward
Vickrum Sukhlani

Retrospective Summary

During this sprint, the team focused on transitioning from the infrastructure we created in project 2, to delivering a functional and deployable point of sale web app system. The team successfully shipped major customer and management workflows, including drink customizations, interactive cart controls, manager drink creation, and the sales report suite.

We did spend a good amount of time at the start trying to correct deployment issues on our host. Most of this early friction was due to our initial file architecture and the specific build and deployment commands we used on Render. Because we settled these issues in this sprint, we should be in good shape for the next sprint as far as worrying about deployability.

Going forward, we recognized that we could be a little more descriptive and granular in our git commits, which would help us keep better track of our incremental updates, bug fixes, and code modifications. At the end of this first sprint, all of our primary product backlog goals and deliverables were met successfully on schedule. For the upcoming sprint, we will likely look more closely into refining our user interfaces, polishing our overall design decisions, conducting thorough testing, and fulfilling crucial accessibility requirements to enhance overall usability. Overall, this sprint laid a robust foundation for our application’s ongoing growth and prepared us well for the upcoming phase of development.we could be a little more descriptive in our commits, to keep better track of our updates. At the end of this first sprint, all of our backlog goals were met.

Product Backlog

ID	User Story Description	Priority	Dependencies	Story Points	Status
US-01	As a developer, I want to set up the project skeleton, index views, node modules, and update deployment ports so the base app runs cleanly.	High	None	5	Completed
US-02	As a user, I want a menu interface with an appealing GUI so I can navigate available items visually.	High	US-01	3	Completed
US-03	As a customer, I want to view drink images, select customizations , and navigate a streamlined checkout flow.	High	US-02	8	Completed
US-04	As a customer, I want quality-of-life checkout fixes and extra topping options during checkout.	Medium	US-03	3	Completed
US-05	As a customer,	Medium	US-03	3	Completed

	I want interactive quantity controls in the cart view so I can edit item counts before ordering.				
US-06	As a staff member, I want an orders page listing the 25 most recent orders (with drinks, quantities, unit prices, and totals) linked from the navbar.	High	US-03	5	Completed
US-07	As a developer, I want to remove leftover starter code and unneeded files to keep the POS codebase clean.	Low	US-01	1	Completed
US-08	As a customer, I want my transaction history and order details to include custom drink selections on the backend.	Medium	US-03, US-06	5	Completed
US-09	As a store manager, I want to create	High	US-03	5	Completed

	new drinks directly from the manager dashboard.				
US-10	As a store manager, I want a dedicated sales report tab to generate sales performance reports.	High	US-06, US-09	5	Completed
US-11	As a team member, I want a central project portal page to access project navigation and management tools.	Low	US-01	2	Completed

Sprint Backlog


-

Story ID	User Story Description	Story Points	Assignee	Actual Time (Hours)	Status
US-01	Set up project skeleton, index views, node modules, update Render ports	5	Joaquin Zapata	6 hrs	Completed
US-02	Menu interface with appealing GUI for visual item navigation	3	Vincent Yen	4 hrs	Completed
US-03	Customer drink image viewing, customization dialog, streamlined checkout	8	Vincent Yen	4 hrs	Completed
US-04	Quality-of-life checkout fixes and extra topping options	3	Vincent Yen	3 hrs	Completed
US-05	Interactive quantity controls in cart view	3	Ryan Kappil	3 hrs	Completed
US-06	Staff orders page listing 25 recent orders (linked in navbar)	5	Ryan Kappil	5 hrs	Completed


US-07	Remove starter code and unneeded files	1	Vickrum Sukhlani	2 hrs	Completed
US-08	Transaction history & order details save custom drinks in backend	5	Landon Ward	5 hrs	Completed
US-09	Store manager drink creation from manager dashboard	5	Vickrum Sukhlani / Landon Ward	6 hrs	Completed
US-10	Manager dedicated sales report tab for performance reports	5	Ryan Kappil	5 hrs	Completed
US-11	Central project portal page for navigation and project tools	2	Vickrum Sukhlani	2 hrs	Completed
TOTAL	All Sprint 1 Deliverables	45	Team 80	45 hrs	100% Completed

Burndown Charts

Sprint Burndown Chart

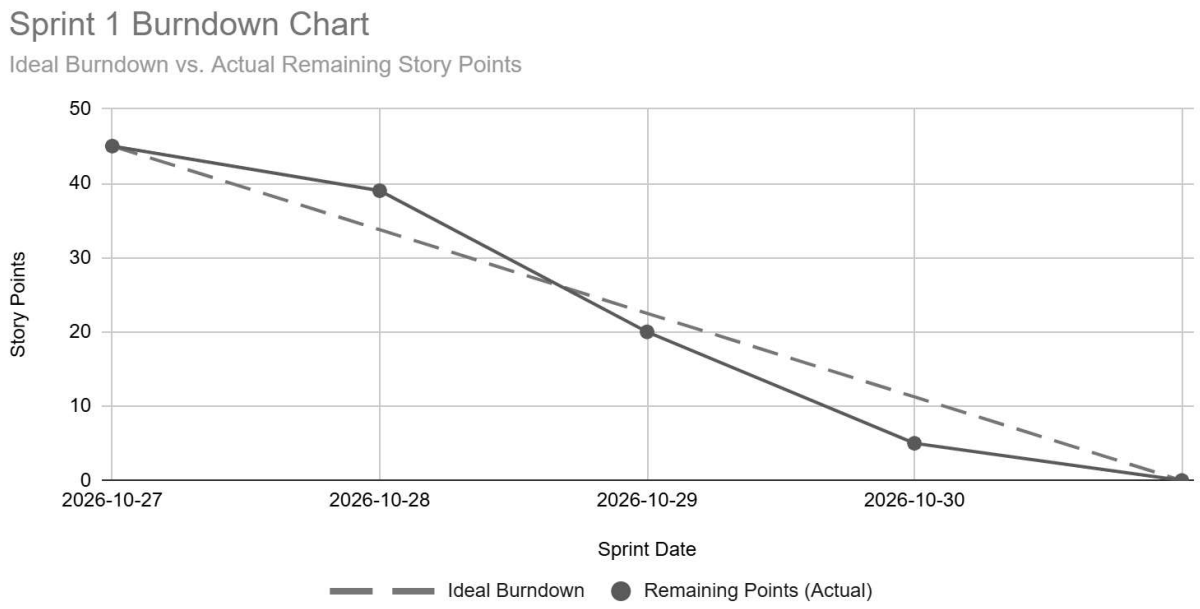

Product Burndown Chart

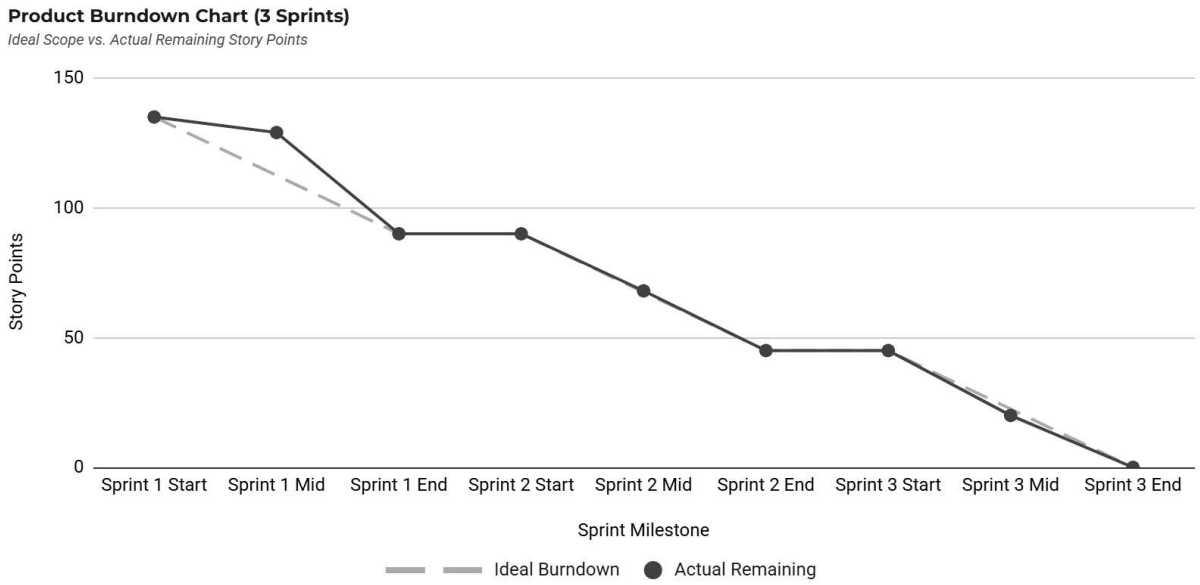

Sprint Test Plan

This sprint plan covers the customer-facing drink-ordering flow: browsing categories, customizing drinks, reviewing cart prices, confirming a demo order, and starting a fresh order. The application uses Express and EJS, reads menu items from PostgreSQL, and stores cart and receipt state in browser sessionStorage.

Testing includes category and drink information, images, customizations, cart behavior, checkout totals, confirmation and reset, empty-cart and storage-error states, responsive layout, keyboard use, and basic screen-reader support. Payment processing, kitchen or POS submission, authentication, durable order records, load testing, penetration testing, database performance testing, and changes to production data are outside this sprint's scope. The confirmation is front-end-only and stored in the browser session.

Test approach and setup

Run manual functional tests against a local app or non-production deployment connected to a test PostgreSQL database. Begin with desktop Chromium, then repeat the critical flows in Firefox and a mobile browser if available. Use a fresh browser tab or clear the app's session storage between independent runs. The menu database should have at least one drink in each available category, with a valid name, description, and price. Record each test drink's displayed base price before checking totals. Session storage should be enabled for normal runs; use a browser profile that blocks storage for the storage-error case.

The current package.json has no test scripts, so record a manual test pass. The checkout confirmation and reset flow has not yet had an end-to-end browser walkthrough, so run the checkout and reset cases early in the sprint.

Functional test scenarios

TC-01, P1: Open the menu with the database available. Verify that categories appear as a vertical list with representative images and that drinks remain hidden until a category is selected.

TC-02, P1: Select a category, switch to another using the top category tabs, and return to all categories. Verify that the selected drinks appear, the horizontal tabs remain visible, the active category is indicated, and the return control restores the category list.

TC-03, P1: Browse each category and inspect the drink cards, then open a drink's customization dialog. Verify that cards show the correct name, description, image, and base price; the dialog shows the selected drink and image; and it can be closed with its close control, a backdrop click, or Escape.

TC-04, P0: Change sugar and ice levels without selecting toppings, add the drink, and review it. Verify that the selections appear on the order, remain free, and leave the drink price equal to its base price.

TC-05, P0: Select each $0.50 topping individually, then select Cheese foam individually. Verify that each $0.50 topping raises the drink price by exactly $0.50, Cheese foam raises it by exactly $1.00, and checkout names each selected topping and shows its price. The $0.50 toppings are Boba, Grass jelly, Pudding, Aloe vera, Lychee jelly, Coconut jelly, and Crystal boba.

TC-06, P0: Select multiple toppings on one drink, including options from both price tiers. Verify that the preview, per-drink price, line total, and order total equal the base price plus the selected topping prices, multiplied by quantity where applicable.

TC-07, P1: Add the same drink twice with identical sugar, ice, and toppings, then add it again with one customization changed. Verify that identical configurations merge and increment quantity, while a changed configuration creates a separate line with its own correct price and customizations.

TC-08, P0: Review multiple drinks with different customizations, navigate from the menu to checkout, and refresh checkout in the same tab. Verify that every line includes the drink, quantity, sugar, ice, paid toppings, base price, add-on subtotal, per-drink price, and line total, and that the order total is correct. Verify that the cart survives same-tab navigation and refresh.

TC-09, P0: Click **Confirm order** with a non-empty cart, then refresh checkout. Verify that confirmation appears, the receipt keeps the ordered items and price details, the active cart badge is zero, and the demo-session receipt survives refresh in the same tab.

TC-10, P0: From the receipt, click **Start a new order**, add a different drink, and return to checkout. Verify that the app returns to the menu, clears the previous cart and receipt, and shows only the new drink at checkout.

TC-11, P1: Open checkout with an empty cart. Verify that the empty-cart message and browse link appear and that totals and confirmation or start-over actions are hidden.

TC-12, P1: Try to add a drink while session storage is unavailable. Verify that a useful error appears and the app does not claim the drink was added or the order confirmed. After restoring storage and reloading, verify that ordering works.

TC-13, P2: Load malformed or outdated cart data in session storage and open checkout. Verify that the app handles it safely, shows an empty order instead of crashing, and does not display corrupted item content.

TC-14, P1: Use the menu and checkout at a narrow mobile width, including the horizontal category tabs and topping options. Verify that content remains readable and operable without page-level horizontal overflow, and that tabs and topping choices can be reached and selected.

TC-15, P2: Navigate with a keyboard and, if available, inspect the dialog and status announcements with a screen reader. Verify visible focus indicators, keyboard operation of all controls, a useful dialog name, and announcements for checkout updates and order confirmation.

TC-16, P1: Stop or misconfigure the test database, request the menu, restore the connection, and retry. Verify that the app presents its menu-load error instead of a broken or misleading menu, then loads normally after the database is restored.

Execution, defects, and sign-off

Run the sprint tests in this order: first verify that the app starts, the test database responds, and the menu renders; then run TC-01 through TC-07 for core ordering and exact price calculations; next run TC-08 through TC-10 for checkout, confirmation, refresh, and start-over; then run TC-11 through TC-16 for resilience, accessibility, and device coverage. Rerun failed cases after fixes and review open defects before sign-off.

Treat a failure to complete the core order flow, an incorrect displayed price, a lost order line or customization, or corrupted receipt/cart state as **P0, a release blocker**. Treat a broken major category, customization, checkout, or supported-device flow with a workaround as **P1, high priority**. Treat visual, copy, or minor accessibility issues that do not prevent ordering or cause an incorrect total as **P2, normal priority**. For each defect, record its test ID, browser or device, build or commit, setup, steps, expected and actual results, and a screenshot or console output when useful.

The sprint is ready to sign off when all P0 and P1 cases pass on the primary browser, no P0 or P1 defects remain open, tested prices match the base price plus paid toppings in integer cents, and sugar and ice remain free. Confirmation and start-over must pass, including refresh and creating a new order after reset. P2 failures should be fixed or explicitly accepted and recorded. The team should also record the tested build, browser and device coverage, case results, and remaining risks.

For the test run record, capture the date, build or commit, browser or device, tester, pass/fail/blocked results, and related defects for each run. No tests have been run; this is the plan only.

Next Sprint's SCRUM Meeting Schedule

Our team plans to hold at least three SCRUM meetings during Sprint 2 to discuss development progress, address technical challenges, and coordinate responsibilities.

1. **SCRUM Meeting 1 – Sprint Planning:** Review Sprint 1 accomplishments and user study feedback, identify remaining project requirements, and assign responsibilities for the cashier screen, kitchen display, inventory management, and external API integrations.
2. **SCRUM Meeting 2 – Progress Check-In:** Discuss progress on the new interfaces, review PostgreSQL integration, evaluate external API implementation, and identify any technical blockers. Review accessibility improvements and customer interface feedback.
3. **SCRUM Meeting 3 – Sprint Review:** Evaluate completed features, test integration between the customer kiosk, cashier screen, kitchen display, and manager dashboard, and address outstanding issues. Prepare for the Sprint 2 GitHub release, written materials, and mid-project presentation.

Additional meetings will be scheduled as needed to resolve issues and ensure timely completion of sprint deliverables.

Appendix 1: SCRUM Meeting Agendas and Minutes

SCRUM Meeting 1 for 80° Boba
Prepared by: Ryan Kappil
Meeting Date: 10/28/26

Meeting Attendees

1. Ryan Kappil
2. Joaquin Zapata
3. Vincent Yen
4. Landon Ward
5. Vickrum Sukhlani

Meeting Agenda Items

- Discuss Sprint 1 MVP requirements and assign development responsibilities
- Plan the customer ordering interface, manager dashboard, and PostgreSQL integration
- Establish the Express/EJS application structure and development workflow

Status Update Since Last Meeting

Accomplishments:

- Established the initial development goals and identified the main features for the Sprint 1 MVP
- Planned the frontend and backend structure for the application

Tasks Completed:

Task Description	**Assigned to**	**Completed? (yes/no)**
Review MVP requirements and plan application structure	Ryan	Yes
Set up Express/EJS project and PostgreSQL configuration	Joaquin	Yes

Before The Next Meeting

Plans:

- Begin developing the customer menu, customization interface, and shopping cart
- Implement the initial manager dashboard and establish database connectivity

Task Assignments:

Task Description	**Assigned to**
Develop customer ordering interface	Vincent
Develop manager dashboard	Vickrum/Landon
Configure PostgreSQL integration	Vickrum/Landon

Minutes from Previous Meeting

The team briefly discussed our initial plans for transitioning the Project 2 POS system into a web-based application for Project 3. We reviewed the project requirements and considered how to divide responsibilities between frontend development, backend functionality, and database integration. We also discussed using Express, EJS, and PostgreSQL to build upon our existing system,

along with the importance of maintaining consistent GitHub contributions and communication throughout the sprint. The team agreed to prioritize the customer ordering interface and manager dashboard to establish a functional MVP before implementing additional features in later sprints.

SCRUM Meeting 2 for 80° Boba
Prepared by: Joaquin Zapata
Meeting Date: 10/29/26

Meeting Attendees

1. Landon Ward
2. Joaquin Zapata
3. Ryan Kappil
4. Vickrum Sukhlani
5. Vincent Yen

Meeting Agenda Items

- Review progress on customer ordering and manager dashboard development
- Discuss PostgreSQL integration, order storage, and remaining MVP functionality

Status Update Since Last Meeting

Accomplishments:

- Developed the categorized drink menu with illustrations, descriptions, and prices
- Implemented drink customization and shopping cart functionality
- Made progress on manager menu management and database integration

Tasks Completed:

Task Description	**Assigned to**	**Completed? (yes/no)**
Develop drink menu and customization options	Vincent	Yes
Implement cart functionality	Ryan/Joaquin	Yes
Develop manager menu management functionality	Vickrum/Landon	Yes

Before The Next Meeting

Plans:

- Complete the checkout process and ensure orders and customizations are saved correctly in PostgreSQL
- Finalize manager sales reporting, transaction history, and application testing

Task Assignments:

Task Description	**Assigned to**
Complete checkout and PostgreSQL order submission	Landon
Implement sales reports and recent-orders functionality	Ryan
Test application features and update project documentation	Joaquin/Vickrum

Minutes from Previous Meeting

During the previous SCRUM meeting, the team discussed the Sprint 1 MVP requirements and established priorities for the customer ordering interface and manager dashboard. The team planned the application structure and divided development responsibilities between frontend and backend functionality. The main goals included implementing the drink menu, customization options, shopping cart, and PostgreSQL integration.

SCRUM Meeting 3 for 80° Boba
Prepared by:
Meeting Date: 10/30/26

Meeting Attendees

1. Landon Ward
2. Joaquin Zapata
3. Ryan Kappil
4. Vickrum Sukhlani
5. Vincent Yen

Meeting Agenda Items

- Review completed Sprint 1 features and test customer and manager functionality
- Identify remaining limitations and prepare for the Sprint 1 GitHub release and Sprint 2 development

Status Update Since Last Meeting

Accomplishments:

- Completed the customer ordering workflow, including drink customization, cart management, checkout, and order confirmation
- Connected order submission to PostgreSQL and saved customizations with order details
- Implemented manager menu management, recent-orders tracking, and date-filtered sales reports
- Updated project documentation and removed unused application files

Tasks Completed:

Task Description	**Assigned to**	**Completed? (yes/no)**
Complete customer checkout and database order submission	Landon	Yes
Implement manager sales report and order history	Ryan	Yes
Update README and organize project files	Vickrum	Yes

Implement automatic inventory reductions	Joaquin	No
Implement manager authentication	Ryan	No

Before The Next Meeting

Plans:

- Begin Sprint 2 development, focusing on the cashier screen, kitchen display, and inventory management
- Plan external API integrations, accessibility improvements, and additional required functionality

Task Assignments:

Task Description	**Assigned to**
Develop cashier screen and kitchen display	Vincent
Implement inventory management, manager authentication and PostgreSQL updates	Ryan/Landon
Begin external API integration and accessibility improvements	Joaquin/Vickrum

Minutes from Previous Meeting

During the previous SCRUM meeting, the team reviewed progress on the customer ordering interface, manager dashboard, and PostgreSQL integration. The team discussed completing the checkout process, saving customer customizations with order transactions, and implementing manager reporting functionality. Remaining tasks included testing frontend and backend integration, finalizing transaction history, and updating project documentation to prepare for the Sprint 1 MVP release.
